ID	Task Name	Duration	Start	Finish	Predecessors
1	**20-049 Beaumont Street Maintenance & Rehab**				
2	**Administrative**				
3	Project Bid	1 day	Thu 10/15/20	Thu 10/15/20	
4	Project Award	1 day	Fri 10/23/20	Fri 10/23/20	
5	Preconstruction Meeting	1 day	Tue 11/10/20	Tue 11/10/20	
6	Submittals	20 days	Tue 11/10/20	Thu 12/10/20	
7	Place Project Info. Signs	2 days	Thu 12/17/20	Fri 12/18/20	
8	Public Notification PCC	1 day	Wed 11/25/20	Wed 11/25/20	
9	Public Notification	2 days	Mon 12/28/20	Tue 12/29/20	
10	Pre-Construction Video	2 days	Fri 12/4/20	Mon 12/7/20	
11	**Construction**				
12	BMP's Install & Maintain	60 days	Mon 11/30/20	Thu 2/25/21	
13	Traffic Control	60 days	Mon 11/30/20	Thu 2/25/21	
14	Notice To Proceed		Mon 12/7/20		
15	**Extra Work PCC**				
16	Saw Cut for PCC	2 days	Mon 11/30/20	Tue 12/1/20	
17	Excavate & Install PCC Cross Gutters	8 days	Mon 11/30/20	Wed 12/9/20	16SS
18	**Street Work**		**Mon 12/7/20**		
19	Weed Kill Cracks All Streets	5 days	Mon 12/7/20	Fri 12/11/20	
20	Rout & Seal Random Cracks ---PRC	17 days	Wed 12/16/20	Wed 1/13/21	
21	Cold Mill 2" Streets	4 days	Mon 1/4/21	Thu 1/7/21	
22	Edge Mill 1" Streets	2 days	Fri 1/8/21	Mon 1/11/21	21
23	R & R 4" Dig Outs	3 days	Mon 1/11/21	Wed 1/13/21	
24	R & R Unsuitable Material	3 days	Mon 1/11/21	Wed 1/13/21	23SS
25	Prelevel 1" Streets (3,100 TONS)	2 days	Thu 1/14/21	Fri 1/15/21	24
26	Overlay 1" & 2" Streets (12,577 TONS)	7 days	Mon 1/18/21	Tue 1/26/21	25
27	Adjust Manholes to Grade ---EBS	2 days	Mon 1/25/21	Tue 1/26/21	26FS-2 days
28	Striping & Markers ---Cal Stripe	3 days	Wed 1/27/21	Fri 1/29/21	
29					
30	**Project Suspension**	**22 days?**	**Fri 1/29/21**	**Mon 3/1/21**	
31	**Slurry Seal Various Streets**				
32	Public notices & Posting ---PCC	5 days	Mon 3/1/21	Fri 3/5/21	
33	Install ARAM (3/8") ---- Man-Hole	2 days	Mon 3/8/21	Tue 3/9/21	32
34	Install Slurry Seal ---PCC	11 days	Mon 3/8/21	Mon 3/22/21	33SS
35	Striping & Markers ---Cal Stripe	3 days	Tue 3/30/21	Thu 4/1/21	34FS+5 days
36	**Project Cleanup Demobilize**	**2 days?**	**Wed 3/31/21**	**Thu 4/1/21**	**35FS-1 day**
37					
38					
39					
40					
41					
42					
43					
44					
45					
46					

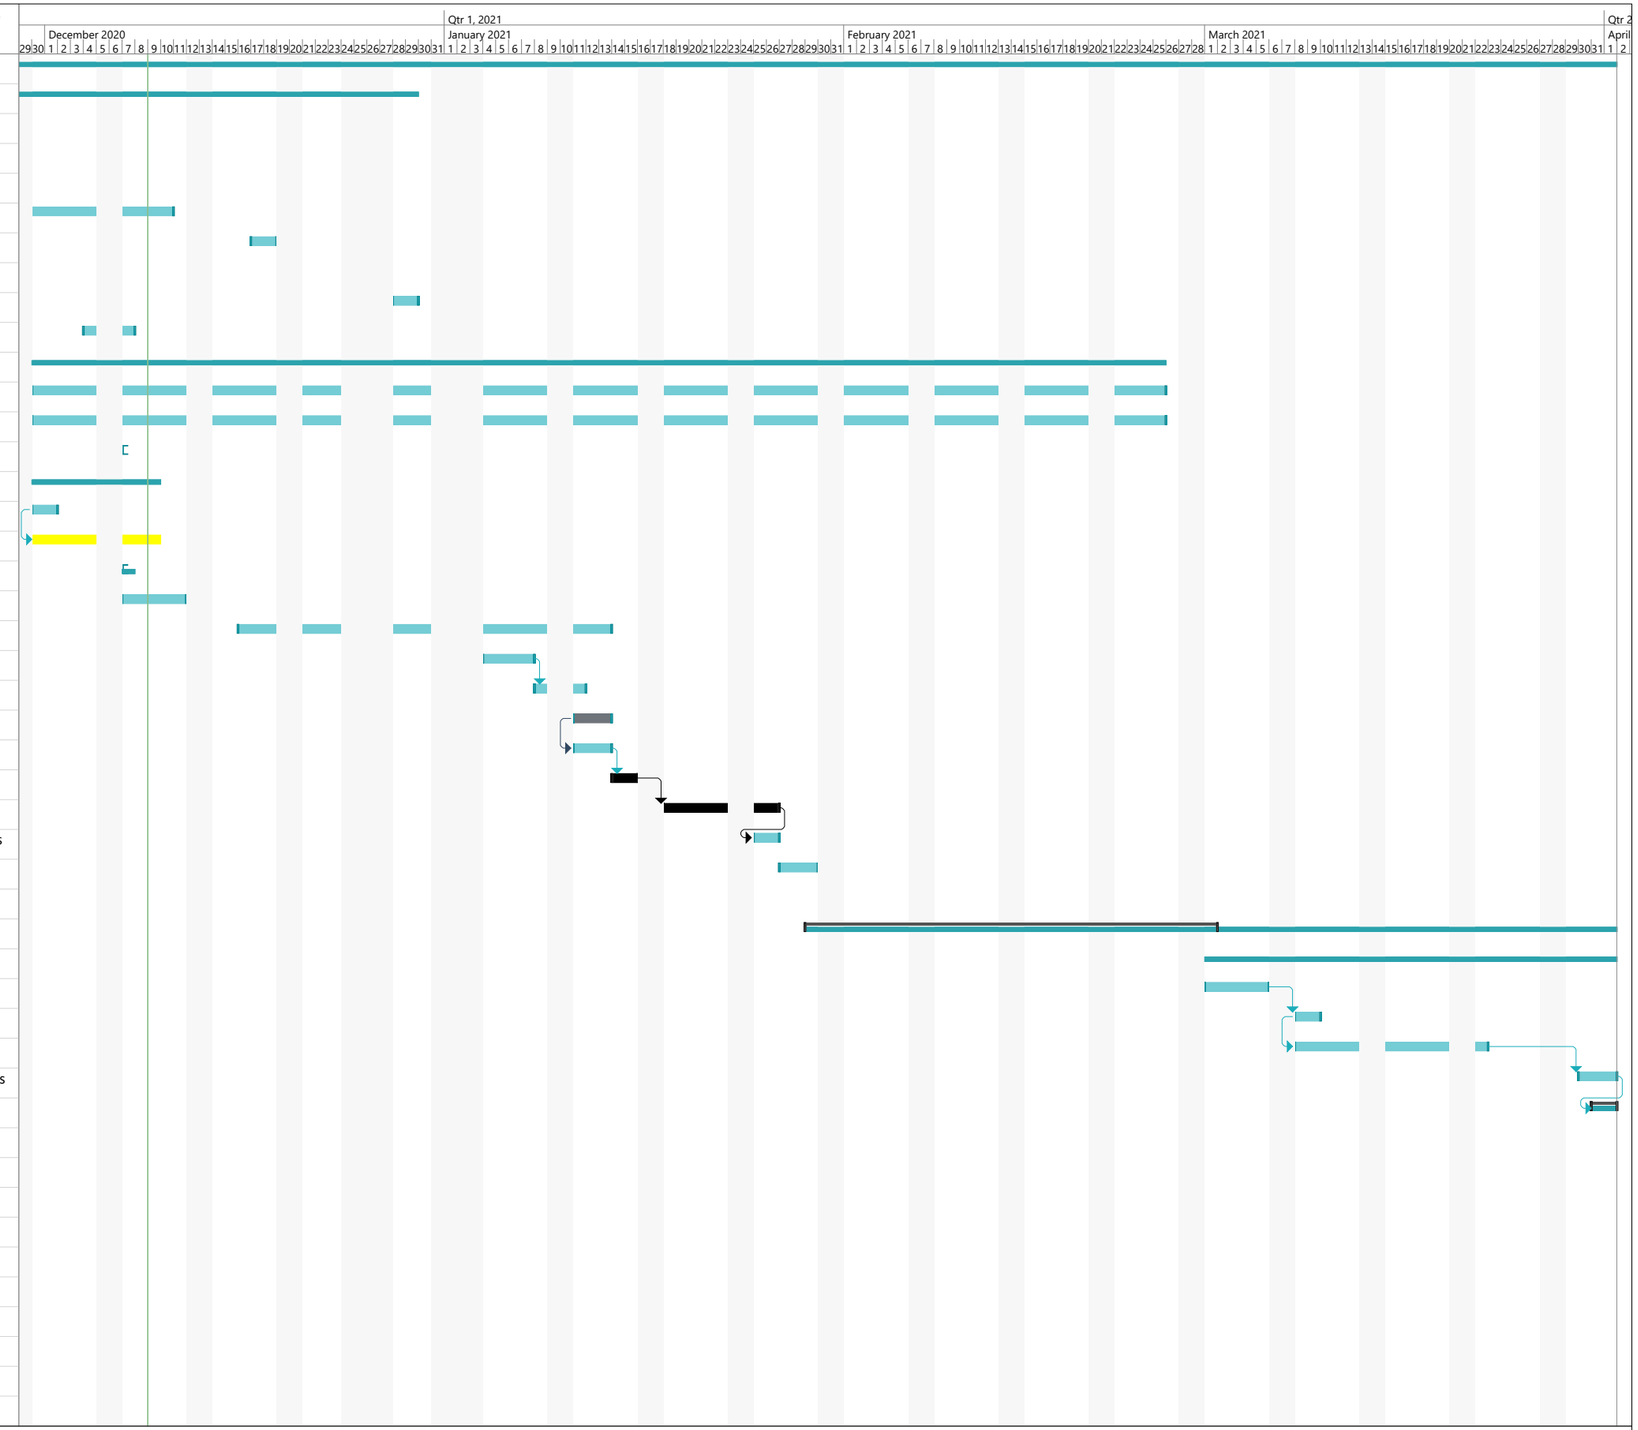

Project: 20-049 Beaumont Street Main
Date: Wed 12/9/20

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
